JCE Infrastructure Pty Ltd

Civil and Hydraulic Engineering | ABN 29 699 165 663

756 Quia Road, Gunnedah NSW 2380 | 0477 207 027 | jayden@jceinfrastructure.com.au | jceinfrastructure.com.au

RFT RETURNABLE DOCUMENTS

Transport Assets Condition Audit & Revaluations 2026/27

Inner West Council | RFT 47-26 | Completed by JCE Infrastructure Pty Ltd, 12/10/2026

Project: Transport Assets Condition Audit & Revaluations 2026/27 | RFT No: RFT 47-26 | Closing: 2:00 pm Wednesday 28/10/2026 (extended from 21/10/2026 by VendorPanel notice of 09/10/2026)

Respondent: JCE Infrastructure Pty Ltd (ABN 29 699 165 663). Completed in the order and wording of Council's Returnable Documents form. Items marked [TBC - Jayden] must be completed before e-signing and saving as PDF.

1 Respondent Declaration

The Respondent named below confirms that having examined and reviewed the entire Request for Tender (RFT) and relying upon its own investigation and due diligence the Respondent accepts the contents of the RFT and submits this Tender to supply the services and perform the work described in the RFT for the fee(s) specified in the Pricing Schedule submitted as part of the Tender. This Tender remains open for acceptance for ninety (90) calendar days from the Tender Closing Date. The Respondent gives the warranties in Council's form (no contact with Council officers other than the Contact Person, no inducements, no canvassing, no collusive tendering), warrants it has no actual or potential conflict of interest except as disclosed in the Tender, and confirms it has reviewed and accepts the NSW Government Model Code of Conduct and Council's Statement of Business Ethics.

Legal Name of Respondent	JCE Infrastructure Pty Ltd
ABN	29 699 165 663
Address of Respondent	756 Quia Road, Gunnedah NSW 2380 [TBC - Jayden: confirm this is the registered address]
Refer enquiries to	Jayden Callen, Director, 0477 207 027, jayden@jceinfrastructure.com.au
Authorised Signatory	Jayden Callen [signature]
Title	Director
Date	[TBC - Jayden: date of lodgement]

2 Pricing Schedule

Item No	Item Particulars	Unit	Quantity	Total ($)
1	Lump Sum for Mandatory asset classes Condition Audit & Comprehensive Revaluation	Lump sum	1	$445,880.00
2	Lump Sum for PCG Meetings (fortnightly to 31 March 2027)	Lump sum	1	$3,240.00
3	Reports (where not included in Item 1)	-	-	Included in Item 1
4	Optional asset class: Lump Sum Kerb/Pram Ramps	Lump sum	1	$54,240.00
5	Optional asset class: Lump Sum Tree Pits & Verge Gardens	Lump sum	1	$34,440.00
6	Optional asset class: Lump Sum Vehicle Crossings	Lump sum	1	$45,440.00
7	Optional asset class: Lump Sum Road & Footpath Markings	Lump sum	1	$39,940.00
8	Optional asset class: Lump Sum Retaining Walls & Comprehensive Revaluation	Lump sum	1	$20,980.00
9	Optional Services A: Lump Sum Transport Asset Prioritisation Analysis	Lump sum	1	$13,680.00

Item No	Item Particulars	Unit	Quantity	Total ($)
10	Other not included above (Please specify)	-	-	Nil
	Total Contract Price (GST Exclusive): mandatory scope, Items 1 to 3 and 10			**$449,120.00**
	GST Amount			**$44,912.00**
	Total Contract Price (GST Inclusive)			**$494,032.00**

Optional Items 4 to 9 are priced separately for Council to select in any combination: $208,720.00 excluding GST for all six ($229,592.00 including GST). The breakdown of Item 1 by stage is in JCE's fee proposal, Section 9.0. [TBC - Jayden: update Items 1 and 4 to 8 if partner quotes (due 21/10/2026) change the provisional sums.]

EXCLUSIONS: State roads and kerb and gutter on State roads (footpaths on State roads are included); assets owned by others; optional items not selected; structural assessment of retaining walls, bridges or structures; underground assets and stormwater drainage; design or delivery of repair, renewal or maintenance works; entry of data into Council's corporate systems (import-ready files are supplied).

3 List of Assumptions

- 1. Award by 30/11/2026, Council data within five (5) business days of award, and Council reviews within five (5) business days; a later award or longer reviews move the program by the same period.
- 2. Field work in daylight hours, Monday to Friday, without lane closures; any lane closure Council requires is arranged by JCE and valued as a variation.
- 3. Artwork is valued at replacement cost on the same basis as other assets; a specialist art market valuation is excluded unless Council asks for it.
- 4. Retaining walls (optional) are assessed from the street and footpath only, as the Scope table describes.
- 5. One round of consolidated Council comments on each draft report; the valuation date is as Council confirms.

4 Requested Amendments to Proposed Contract

Clause No.	Clause Title	Requested Amendment
Schedule 1 (clause 8.3)	Payment Claims	Monthly payment claims against the stage lump sums in the Pricing Schedule (Schedule 1 leaves the claim times blank).
12.7	Insurances (Civil Liability Act)	[TBC - Jayden: delete this row unless you decide to request it] Delete the exclusion of Part 4 of the Civil Liability Act 2002 (NSW), so that proportionate liability applies.
11.3 and Schedule 1	Limitation of Liability	[TBC - Jayden: delete this row unless you decide to request it] Limit liability to the greater of 100% of the Fee and the professional indemnity limit required by the Agreement.

5 Details of Insurance

The Respondent confirms it can provide the insurances required below and acknowledges such insurances will be a requirement of the Agreement. Certificates of currency are attached.

Insurance type	Per incident $A	Aggregate $A	Policy No.	Expiry date	Name of insurer
Public Liability	$20m (JCE holds $10m now and will lift to $20m on award, before the Services commence)	N/A	05-ENG-I-0077656	02/07/2027	Zurich Australian Insurance Limited
Workers Compensation	As per law	As per law	[TBC - Jayden: icare policy no.]	[TBC - Jayden]	icare NSW
Professional Indemnity	$10,000,000	$20,000,000	05-ENG-I-0077656	02/07/2027	Certain Underwriters at Lloyd's (Markel Syndicate 3000)

Insurance type	Per incident $A	Aggregate $A	Policy No.	Expiry date	Name of insurer
Motor Vehicle	Per certificate	Per certificate	[TBC - Jayden: from NRMA certificate 18/09/2026]	[TBC - Jayden]	NRMA Insurance
Contract Insurance	Not applicable (professional services)	-	-	-	-


Conserve Contractor ID	Not registered. JCE will register with BNG Conserve if requested after award (clause 12.6).

6 Proposed Methodology

Methodology to identify works with contract award anticipated in November 2026 and completion no later than 31 March 2027: see the attached JCE fee proposal (JCE_FP_VP527819_Final_RevF.pdf), Section 2.0 (six stages and two Council hold points), Section 2.1 (proposed data capture and GIS system: capture platform, mapping-grade DGPS to 1 m with GPS feature metadata, 5 MP geo-referenced photographs with embedded metadata, segment convention, Excel and ESRI shapefile outputs in MGA Zone 56 GDA2020 with data dictionary and metadata, geometry checks, TechnologyOne and IntraMaps or QGIS compatibility), Section 2.2 (data audit and verification) and Section 2.3 (risks). Optional Service A methodology is in Section 7.0.

7 Proposed Schedule

Schedule to identify works with contract award anticipated in November 2026 and completion no later than 31 March 2027. Start date: award, assumed 30/11/2026. Key milestones: inception and field trial 08/12/2026 to 09/12/2026; pilot 11/01/2027 to 22/01/2027; pilot approval 28/01/2027; network capture 01/02/2027 to 05/03/2027; audit data complete 12/03/2027; draft revaluation 19/03/2027. Report submission and workshop: workshop 24/03/2027. Practical completion: final report and final revaluation report 31/03/2027. Optional Service A by 30/06/2027. Full table in the fee proposal, Section 4.0.

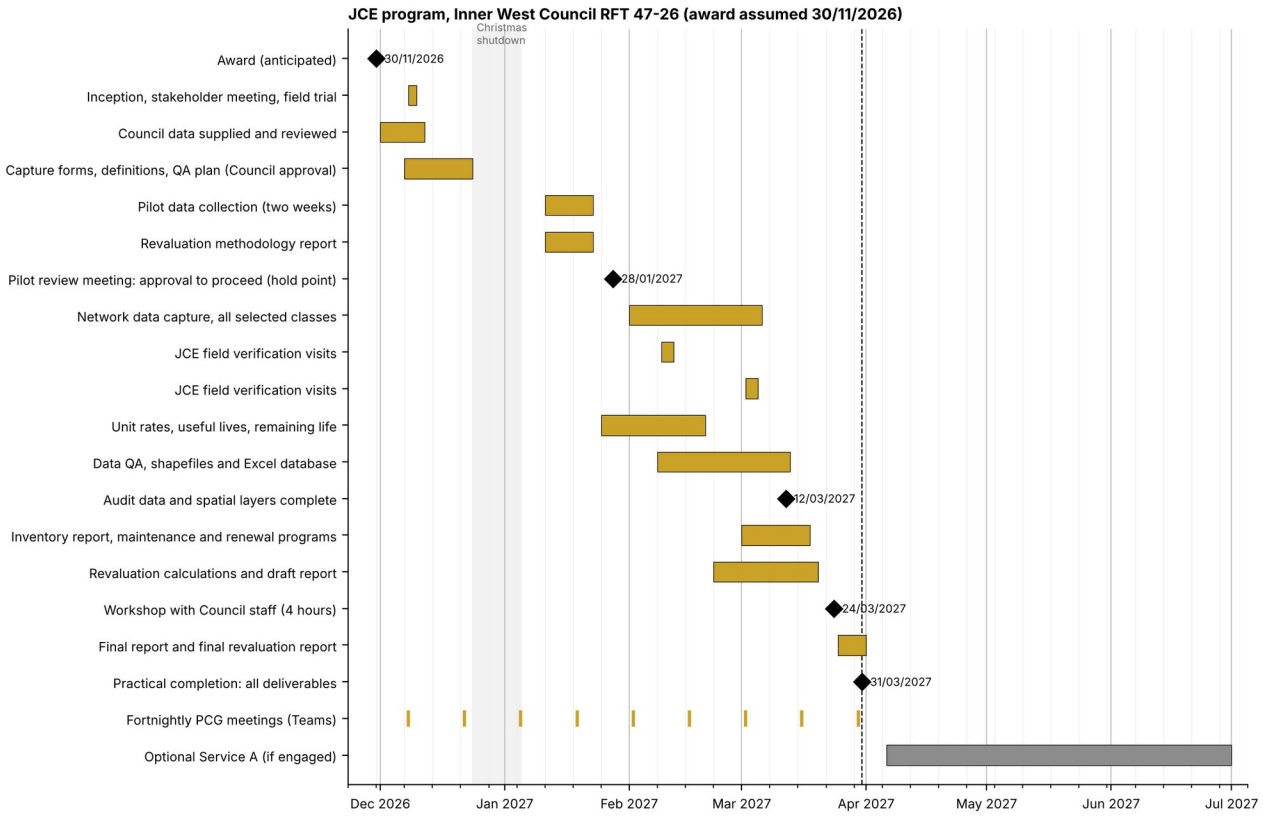

8 Acknowledgement of RFT Addenda

Addenda Number	Brief Description	Date Received
VendorPanel notice (no addendum number)	Closing date extended to 2:00 pm Wednesday 28 October 2026; Council advises no further extensions.	09/10/2026
[TBC - Jayden]	No addenda issued as at 12/10/2026. Re-check VendorPanel (Members > View all Tenders > RFT-47) before lodging and list any received.	

9 Declaration of Site Inspection

The Respondent confirms that it has, of its own accord, inspected the proposed work site (various locations in the Inner West LGA) and has acquired a sound knowledge of the physical characteristics of the site and surrounding areas and any consequential procedures, processes and legislative requirements.

[TBC - Jayden: inspect a representative sample of the network (for example a town centre such as Marrickville or Leichhardt, a residential area and a Council car park) before signing. Record the date and areas here. Do not sign until the inspection is done.]

Signed	[signature] Jayden Callen, Director
Date of inspection	[TBC - Jayden]

10 Company Profile

JCE Infrastructure Pty Ltd is a principal-led civil and hydraulic engineering consultancy based in Gunnedah, NSW, serving councils, developers and consulting firms across NSW and Queensland. The company was incorporated in 2026, building on a design practice operated since March 2024. Its Director, Jayden Callen, BEng (Hons), MIEAust, has more than eight years of experience in Defence infrastructure, land development, roads and pavements, stormwater and water infrastructure, including design management of multidisciplinary teams and subconsultants. JCE works with associates and specialist partners; for this contract it will engage a field data capture partner and a qualified valuer as approved subcontractors.

- **Size:** Director-led company with associates and specialist subconsultants. [TBC - Jayden: number of staff and associates]
- **Corporate structure:** Proprietary limited company; Jayden Callen is Director. [TBC - Jayden: confirm shareholding wording]
- **History:** Design practice from March 2024; incorporated 2026.
- **Expertise:** Civil design and design management, roads and pavements, stormwater and flooding, water and sewer, construction-phase inspection and quality assurance, engineer's estimates and bills of quantities, Civil 3D and GIS data management.
- **Value added:** Principal-led delivery with one point of contact; independent JCE QA of all field data; engineering-based unit rates and remaining lives; practical maintenance and renewal programs; two Council hold points before network capture.

Our organisation has the capacity to deliver the project condition audit data, spatial layers and comprehensive revaluation reports as outlined in the brief by 31/03/2027. [TBC - Jayden: keep this statement only once the data capture partner has committed crews in its quote.]

11 Respondents Experience

[TBC - Jayden: at least three similar projects in the last five years with referees. JCE has none of its own; use the data capture and valuation partners' projects from their quotes (due 21/10/2026), labelled as the partner's projects, with referees who have agreed to be contacted.]

Previous project	Referee contact details
Contract Name: [TBC] Description: [TBC] Location: [TBC] Value: [TBC] Date undertaken: [TBC]	Name: [TBC] Organisation: [TBC] Role: [TBC] Phone: [TBC] Email: [TBC]
Contract Name: [TBC] Description: [TBC] Location: [TBC] Value: [TBC] Date undertaken: [TBC]	Name: [TBC] Organisation: [TBC] Role: [TBC] Phone: [TBC] Email: [TBC]
Contract Name: [TBC] Description: [TBC] Location: [TBC] Value: [TBC] Date undertaken: [TBC]	Name: [TBC] Organisation: [TBC] Role: [TBC] Phone: [TBC] Email: [TBC]

12 Key Personnel

Employee name and position	Years employed	Qualification / experience	Proposed role
Jayden Callen, Director	Since 2024 (practice); 2026 (company)	BEng (Hons) Civil; MIEAust (11036201); 8+ years civil engineering and design management	Project manager; Prime Contractor representative; signs all documents
Sunny Lotay, Associate (Lotay Civil) [TBC - Jayden: confirm]	Associate	NER, RPEng (Vic) [TBC - Jayden: confirm years of experience]	Data QA and GIS outputs
Livio Chiarot, Associate (SCP Consulting) [TBC - Jayden: confirm]	Associate	FIEAust [TBC - Jayden: confirm years of experience]	Independent technical reviewer
[TBC - Jayden: data capture partner field lead]	Partner	[From partner quote]	Field data capture lead
[TBC - Jayden: valuation partner signing valuer]	Partner	[From partner quote]	Revaluation review and sign-off

13 Proposed Subcontractors

Name of proposed subcontractor	Proposed role	Recent experience	Insurances provided
[TBC - Jayden: field data capture partner, from quotes due 21/10/2026]	Field inventory and condition audit, pilot, DGPS and photography, data processing	[From partner quote]	PL $20m; PI $10m; WC as per law [confirm from certificates]
[TBC - Jayden: valuation partner, from quotes due 21/10/2026]	Comprehensive revaluation review and sign-off by a qualified valuer	[From partner quote]	PL $20m; PI $10m; WC as per law [confirm from certificates]

14 Quality Assurance Plan Checklist

Item	Subject	Yes	No
1	Quality Assurance management system as part of the overall management system? Quality Policy JCE-QMS-POL-001 (Rev 1.0, 22/06/2026) attached; document control, QA and certification templates and registers; project QA plan per fee proposal Section 2.2.	X	
2	Accredited to an ISO standard?		X
3	Quality Policy? It has the documented support of the Director (signed 23/06/2026) and relates to JCE's activities and services.	X	
	Reflects the organisation's values and guiding principles? [TBC - Jayden: confirm from policy wording]		
	Guides the setting of quality objectives and targets? [TBC - Jayden: confirm]		

Item	Subject	Yes	No
	Guides monitoring of management practices? [TBC - Jayden: confirm]		
4	Management representative for quality: the Director.	X	
5	Documented evidence (management review minutes, internal audit reports, a typical quality plan)? [TBC - Jayden: tick only what you can attach; a typical project quality plan is the easiest]		
6	Quality principles in training and induction? [TBC - Jayden: confirm JCE-WHS-PRO-008 covers quality]		
7	Procedures for control of quality from subcontractors and suppliers: Quality Policy and JCE-WHS-PRO-009.	X	
8	Corrective action procedure? [TBC - Jayden: confirm]		
9 to 11	Management review of quality principles, regular, with follow-up? Annual policy review (next 22/06/2027). [TBC - Jayden: confirm]		

15 Work Health & Safety (WHS) Checklist

Item	Subject	Yes	No
1	Written WHS policy: JCE-WHS-POL-001 (attached).	X	
	WHS Management System / Manual: JCE WHS Management System 22/06/2026 (contents page attached).	X	
	WHS Management Plan: JCE-WHS-PLN-001 (attached); project plan before site access (clause 18).	X	
2	COVID-19 Safety Plan? [TBC - Jayden]		
3	Health and safety responsibilities identified for all levels (WHS Management Plan).	X	
	WHS Management Plan accredited by a NSW Government agency or third party?		X
4	SWMS for significant-risk work: JCE-WHS-SWMS-001 (attached) with the summary list of procedures from the WHS Management System contents page.	X	
	Staff trained for traffic control and traffic management plans? JCE staff are not traffic controllers; field work near traffic uses accredited controllers to an approved traffic guidance scheme. [TBC - Jayden: attach the data capture partner's TMP example and answer Yes only if it is attached]		
5	WHS training: worker WHS induction (JCE-WHS-PRO-008), training and competency register (JCE-WHS-REG-003), site inspection and site entry procedure (JCE-WHS-PRO-005), pre-site Take-5 risk assessment (JCE-WHS-FRM-002), and project inductions for subcontractors.		
6	WHS induction program: JCE-WHS-PRO-008 (attached).	X	
	Record of inductions: training and competency register JCE-WHS-REG-003.	X	
7	Register of workplace injuries: incident register JCE-WHS-REG-002.	X	
	Incident investigation procedure, with incident report form JCE-WHS-FRM-001 (attached).	X	
8	Regular WHS inspections at worksites, with form: pre-site Take-5 risk assessment JCE-WHS-FRM-002 (attached). [TBC - Jayden: confirm Yes]		
9	Hazard reporting procedure: incident, hazard and near-miss report form JCE-WHS-FRM-001.	X	
10	Employees involved in WHS decisions (consultation procedure JCE-WHS-PRO-001).	X	
11	Recording and analysing WHS statistics: incident register JCE-WHS-REG-002.	X	
12	SafeWork NSW (WorkCover) prohibition or improvement notices or fines in the past 12 months? [TBC - Jayden]		
	Any convictions? [TBC - Jayden]		
13	Assessment of subcontractors' WHS capability: JCE-WHS-PRO-009 (attached).	X	
14	People or resources nominated for the listed WHS duties: the Director.	X	

16 Industrial Relations Checklist

Item	Subject	Yes	No
1	Persons currently employed: Full time [TBC - Jayden]; Part-time [TBC]; Casual [TBC]		
2	Persons working directly on this contract: Full time [TBC - Jayden]; Part-time [TBC]; Casual [TBC] (plus partner field crews)		

Item	Subject	Yes	No
3 to 14	IR policy, qualified IR personnel, workplace contracts, contingency plans, legal employment and tax compliance, long service leave, IR record, grievance procedure, subcontractor IR compliance, coordination with unions, lost-time disputes, current disputes. [TBC - Jayden: answer each Yes or No on Council's form; no IR disputes are known to this draft]		

17 Sustainability Questionnaire

Item	Subject	Yes	No
1	Documented procedures for environmental incidents: Environmental Policy JCE-ENV-POL-001 and incident reporting (JCE-WHS-FRM-001). [TBC - Jayden: confirm]	X	
2	Aware of the requirement to prepare, implement and review a project EMP and respond to Council audits.	X	
3	Any offence, notice or licence action under NSW environmental legislation? [TBC - Jayden]		
4	Environmental Management System? Environmental Policy in place. [TBC - Jayden: answer]		
	If Yes, is the system certified?		X
5	Advise on or work on upstream fossil fuel projects in Australia? [TBC - Jayden]		

18 Modern Slavery Act Checklist

Part A	Response
1. Subject to reporting under the Modern Slavery Act 2018 (Cth) or UK Act 2015?	No: JCE is below the reporting threshold. [TBC - Jayden: confirm]
2. How the business manages modern slavery risk	Some processes have been introduced and a rollout plan is underway (Modern Slavery Policy JCE-WHS-POL-003, attached).
3. Willing to work with Council and the NSW Government?	Yes

Part B	Response
B1.1 Operations and countries	JCE Infrastructure Pty Ltd provides professional civil and hydraulic engineering services in Australia, delivered by its Director with associates and Australian subconsultants.
B1.2 Supply chain	Mainly software, IT equipment, vehicles, insurance and Australian subconsultants (for this contract, an Australian data capture firm and an Australian valuer).
B1.3 How risks are identified	Under the Modern Slavery Policy (JCE-WHS-POL-003) and subconsultant onboarding checks under JCE-WHS-PRO-009; risks assessed as low.
B1.4 Risks in the services for this RFT	No specific risk identified. The main exposure is IT and field equipment (tablets, cameras, GPS receivers) bought by subcontractors, which JCE will ask them to cover in their own policies.
B2.1 How risk is addressed	Modern Slavery Policy; subconsultant onboarding checks; subcontractors on this contract confirm compliance in writing before engagement.
B2.2 Member of or certified by a social or workforce audit body?	No
B2.3 Plans if no measures	Not applicable: measures are in place.
B2.4 Further information	Modern Slavery Policy JCE-WHS-POL-003 attached.
B3.1 Tracking effectiveness	Annual policy review by the Director; subcontractor confirmations kept on file.
B3.2 Engaging suppliers for this RFT	Each subcontractor confirms it complies with JCE's Modern Slavery Policy, or provides its own, before engagement; the subcontract requires it to notify JCE of any risk identified.

19 Environmental, Local and Aboriginal & Torres Strait Islander Checklist

Schedule 1 of the RFT does not tick this checklist, but it is an evaluation criterion, so it is completed.

Item	Subject	Yes	No
1	Local business? JCE is based in Gunnedah, NSW.		X
2	Employ people who reside in the Inner West area?		X
3	Aboriginal or Torres Strait Islander business? Approximate number of staff who identify: [TBC - Jayden]		
4	Social enterprise? [TBC - Jayden]		
5	Employ persons with a disability? [TBC - Jayden]		

20 Other

Requested Information	Attachments to this Tender (all referencing RFT 47-26)
Response	1. JCE_FP_VP527819_Final_RevF.pdf: fee proposal (methodology, GIS system, QA, program and Gantt chart, team, Optional Service A, pricing basis) 2. JCE Capability Statement - Councils.pdf 3. Callen-Pell_NER-02_Detailed_CV.pdf 4. Certificate of currency (PI and PL, 13/07/2026); workers compensation certificate [TBC - Jayden]; motor vehicle certificate (NRMA, 18/09/2026) 5. JCE-QMS-POL-001 Quality Policy 6. JCE-WHS-POL-001 WHS Policy; JCE_WHS_Management_System_2026-06-22 (contents page); JCE-WHS-PLN-001 WHS Management Plan; JCE-WHS-SWMS-001; JCE-WHS-PRO-008; JCE-WHS-PRO-009; JCE-WHS-FRM-001; JCE-WHS-FRM-002 7. JCE-WHS-POL-003 Modern Slavery Policy 8. JCE-ENV-POL-001 Environmental Policy 9. Partner company profiles, CVs and certificates of currency [TBC - Jayden: from quotes]
